ID		Task Name	Duration	Start	Finish	Predecessors	% Complete	Milestone	Resource Names	Deadline
1	✓	Online group meeting session 1	1 day	Sun 3/8/26	Sun 3/8/26		100%	Yes	Team	NA
2	✓	Meeting session 1documentation	1 day	Mon 3/9/26	Mon 3/9/26	1	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
3	✓	Project Exercise one	1 day	Sat 3/28/26	Sat 3/28/26	2	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
4	✓	System name determination	4 days	Fri 4/10/26	Wed 4/15/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
5	✓	Requirements gathering (very	4 days	Tue 3/17/26	Fri 3/20/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
6	✓	Brainstorming documentation	14 days	Mon 3/30/26	Thu 4/16/26	2	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
7	✓	Feasibility Analysis	30 days	Tue 3/17/26	Fri 5/29/26	6	100%	No	ali,hamed,mohammad hossein,sajad,abolfazl	NA
8	✓	Technical Analysis	3 days	Wed 4/29/26	Tue 6/2/26	7	100%	No	abolfazl	NA
9	✓	Organizational Analys	5 days	Mon 4/27/26	Thu 6/4/26	7	100%	No	ali	NA
10	✓	Economical analysis	3 days	Mon 4/27/26	Tue 6/2/26	7	100%	No	hamed	NA
11	✓	Make Project WBS	68 days	Tue 4/14/26	Thu 7/16/26		100%	No	sajad	NA
12	✓	Online group meeting session 2	1 day	Fri 4/10/26	Fri 4/10/26		100%	Yes	Team	NA
13	✓	Git Lab initialization	3 days	Wed 4/15/26	Fri 4/17/26	4	100%	No	sajad	NA
14	✓	Create Repository	1 day	Mon 4/20/26	Mon 4/20/26	13	100%	No	sajad	NA
15	✓	Connect local folders to repository	1 day	Tue 4/21/26	Tue 4/21/26	14	100%	No	sajad	NA
16	✓	Add members to the repository	1 day	Wed 4/22/26	Wed 4/22/26	15	100%	No	sajad	NA
17	✓	Make Project standar	7 days	Thu 4/16/26	Fri 4/24/26		100%	No	sajad	NA
18	✓	Make team charter	21 days	Sat 4/25/26	Fri 5/22/26		100%	No	sajad	NA
19	✓	Advanced Requirements gathering (Based on	20 days	Mon 3/23/26	Fri 4/17/26	5	100%	No	abolfazl	NA
20	✓	Make a Gantt chart for the team	64 days	Mon 4/20/26	Thu 7/16/26	11	100%	No	abolfazl	NA
21	✓	Risk Analysis of the project	14 days	Sat 4/25/26	Wed 5/13/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
22	✓	Make System request	14 days	Thu 4/23/26	Tue 5/12/26	3	100%	No	hamed	NA
23	✓	Analyse previous projects by students	1 day	Wed 4/22/26	Wed 4/22/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
24	✓	Network diagram implementation	64 days	Mon 4/20/26	Thu 7/16/26	11	100%	No	abolfazl	NA
25	✓	Problem analysis	14 days	Sat 4/25/26	Wed 5/13/26		100%	No	mohammad hossein	Wed 5/13/26
26	✓	Root cause analysis	14 days	Sat 4/25/26	Wed 5/13/26	19	100%	No	mohammad hossein	Wed 5/13/26
27	✓	Business process analysis	11 days	Sun 5/10/26	Fri 5/22/26	19	100%	No	mohammad hossein	Sat 5/23/26
28	✓	Informal benchmarki	11 days	Sun 5/10/26	Fri 5/22/26		100%	No	mohammad hossein	NA
29	✓	Online group meeting session 3	1 day	Wed 4/22/26	Wed 4/22/26		100%	Yes	Team	NA
30	✓	Make Meeting Session 3 docs	1 day	Thu 4/23/26	Thu 4/23/26	29	100%	No	sajad	NA
31	✓	Outcome Analysis	1 day	Sat 4/25/26	Sat 4/25/26		100%	No	abolfazl	NA
32	✓	Project work-plan table (dates,progression	4 days	Tue 4/28/26	Fri 5/1/26		100%	No	sajad	NA
33		Use-case diagram making	7 days	Sat 5/2/26	Tue 6/9/26	19	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Wed 5/6/26
34	✓	Project Size and Effort Estimation (Use-case	58 days	Mon 4/27/26	Wed 7/15/26	19	100%	No	sajad	NA
35	✓	Activity diagrams making	4 days	Sun 5/10/26	Wed 5/13/26	33	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Wed 5/13/26
36	✓	Write use-case descriptions	15 days	Sun 5/10/26	Thu 5/28/26	33,35	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Fri 5/29/26
37	✓	Create Concept Map	2 days	Mon 6/8/26	Tue 6/9/26	19	100%	No	ali	NA
38	✓	Learn required programming skills	94 days	Mon 3/9/26	Thu 7/16/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
39	✓	Review WBS 25, 27; Review-01	5 days	Tue 6/9/26	Tue 6/16/26	33,35	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
40	✓	Review WBS 18, 6 11; Review-02	5 days	Sun 5/17/26	Fri 5/22/26	26,7,8,9,10	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
41	✓	Review WBS 28; Review-03	9 days	Wed 5/20/26	Mon 6/1/26	36	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Mon 6/1/26
42	✓	Perform a V&V meeting for activity diagram and use-case diagrams	2 days	Tue 6/9/26	Thu 6/11/26	36,33,35	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Thu 6/11/26
43	✓	Emergency Meeting (S4) + Docs	1 day	Wed 5/27/26	Wed 5/27/26		100%	Yes	Team	NA
44	✓	Make Project's United Document	1 day	Fri 6/5/26	Fri 6/5/26		100%	No	sajad	NA
45	✓	UI implementation planning	2 days	Sat 5/30/26	Mon 6/1/26		100%	No	sajad	NA
46	✓	Front-End implementation	5 days	Mon 6/1/26	Fri 6/5/26	5,33,35,36	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
47	✓	Fix & update functional models	4 days	Sun 6/7/26	Wed 6/10/26	33,35,36	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Wed 6/10/26
48	✓	CRC Cards	2 days	Sat 6/13/26	Mon 6/15/26		100%	No	abolfazl	NA
49	✓	CRC V&V Meeting Session + determine classes & objects	2 days	Thu 6/18/26	Fri 6/19/26	48	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
50	✓	Class Diagrams	3 days	Mon 6/22/26	Wed 6/24/26	48,49	100%	No	hamed	Wed 6/24/26
51	✓	Object Diagrams	2 days	Thu 6/25/26	Fri 6/26/26	50	100%	No	abolfazl	NA
52	✓	Improve Frontend	12 days	Fri 6/12/26	Sun 6/28/26		100%	No	abolfazl,ali,hamed,mohammad hossein	Sun 6/28/26
53	✓	Initial System proposal writing	11 days	Mon 5/25/26	Mon 6/8/26	22,18,6	100%	No	ali,sajad	NA
54	✓	Update Login Act diag based on new	4 days	Mon 6/15/26	Thu 6/18/26		100%	No	sajad	Thu 6/18/26
55	✓	Find an external host and implement the website	2 days	Tue 6/16/26	Wed 6/17/26		100%	No	mohammad hossein,sajad	NA
56	✓	Initial database desig	6 days	Tue 6/16/26	Tue 6/23/26	33,35,36,45	100%	No	abolfazl	NA
57	✓	Initial Backend implementation	6 days	Mon 6/22/26	Mon 6/29/26		100%	No	hamed	NA
58	✓	Improve Class diagra	3 days	Thu 6/25/26	Mon 6/29/26	50	100%	No	hamed,sajad	NA
59	✓	Sequence diagrams	3 days	Thu 7/2/26	Mon 7/6/26		100%	No	hamed	Mon 7/6/26
60	✓	Communication Diagram	5 days	Tue 7/7/26	Mon 7/13/26	59	100%	No	mohammad hossein	Fri 7/10/26
61	✓	Behavioral state machine	5 days	Tue 7/14/26	Mon 7/20/26	59,60	100%	No	mohammad hossein	NA
62	✓	CRUDE analysis	2 days	Mon 7/6/26	Tue 7/7/26		100%	No	abolfazl	NA
63	✓	Make database schem	2 days	Tue 6/30/26	Wed 7/1/26	50,57	100%	No	abolfazl	NA
64	✓	Fix and update Functional models	10 days	Sat 7/4/26	Thu 7/16/26	35	100%	No	ali,sajad	NA
65	✓	Do the exercises teacher sent	5 days	Sat 7/4/26	Thu 7/9/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
66	✓	Improve Economic feasibility	2 days	Wed 7/8/26	Thu 7/9/26	10	100%	No	hamed	NA
67	✓	Stable database version	4 days	Fri 7/3/26	Wed 7/8/26	48	100%	No	abolfazl	NA
68	✓	Backend Implementation	6 days	Sun 7/5/26	Fri 7/10/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
69	✓	Finish system proposa	8 days	Tue 6/9/26	Thu 6/18/26	53	100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	NA
70	✓	Part one of System proposal	2 days	Tue 7/7/26	Wed 7/8/26		100%	No	ali,hamed,sajad	Wed 7/8/26
71	✓	Part two of the system proposal	2 days	Wed 7/8/26	Thu 7/9/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Thu 7/9/26
72	✓	Part three of the system proposal	2 days	Thu 7/9/26	Fri 7/10/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Fri 7/10/26
73	✓	Part four of the system proposal	2 days	Tue 3/10/26	Wed 3/11/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Sat 7/11/26
74	✓	Part five of the system proposal	3 days	Wed 3/11/26	Fri 3/13/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Sat 3/14/26
75	✓	Part six of the system proposa	4 days	Mon 7/13/26	Thu 7/16/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Thu 7/16/26
76	✓	Fix Frontend issues	6 days	Sat 7/11/26	Fri 7/17/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Sun 7/19/26
77	✓	Test backend for issu	2 days	Fri 7/17/26	Sun 7/19/26		100%	No	abolfazl,ali,hamed,mohammad hossein,sajad	Sun 7/19/26

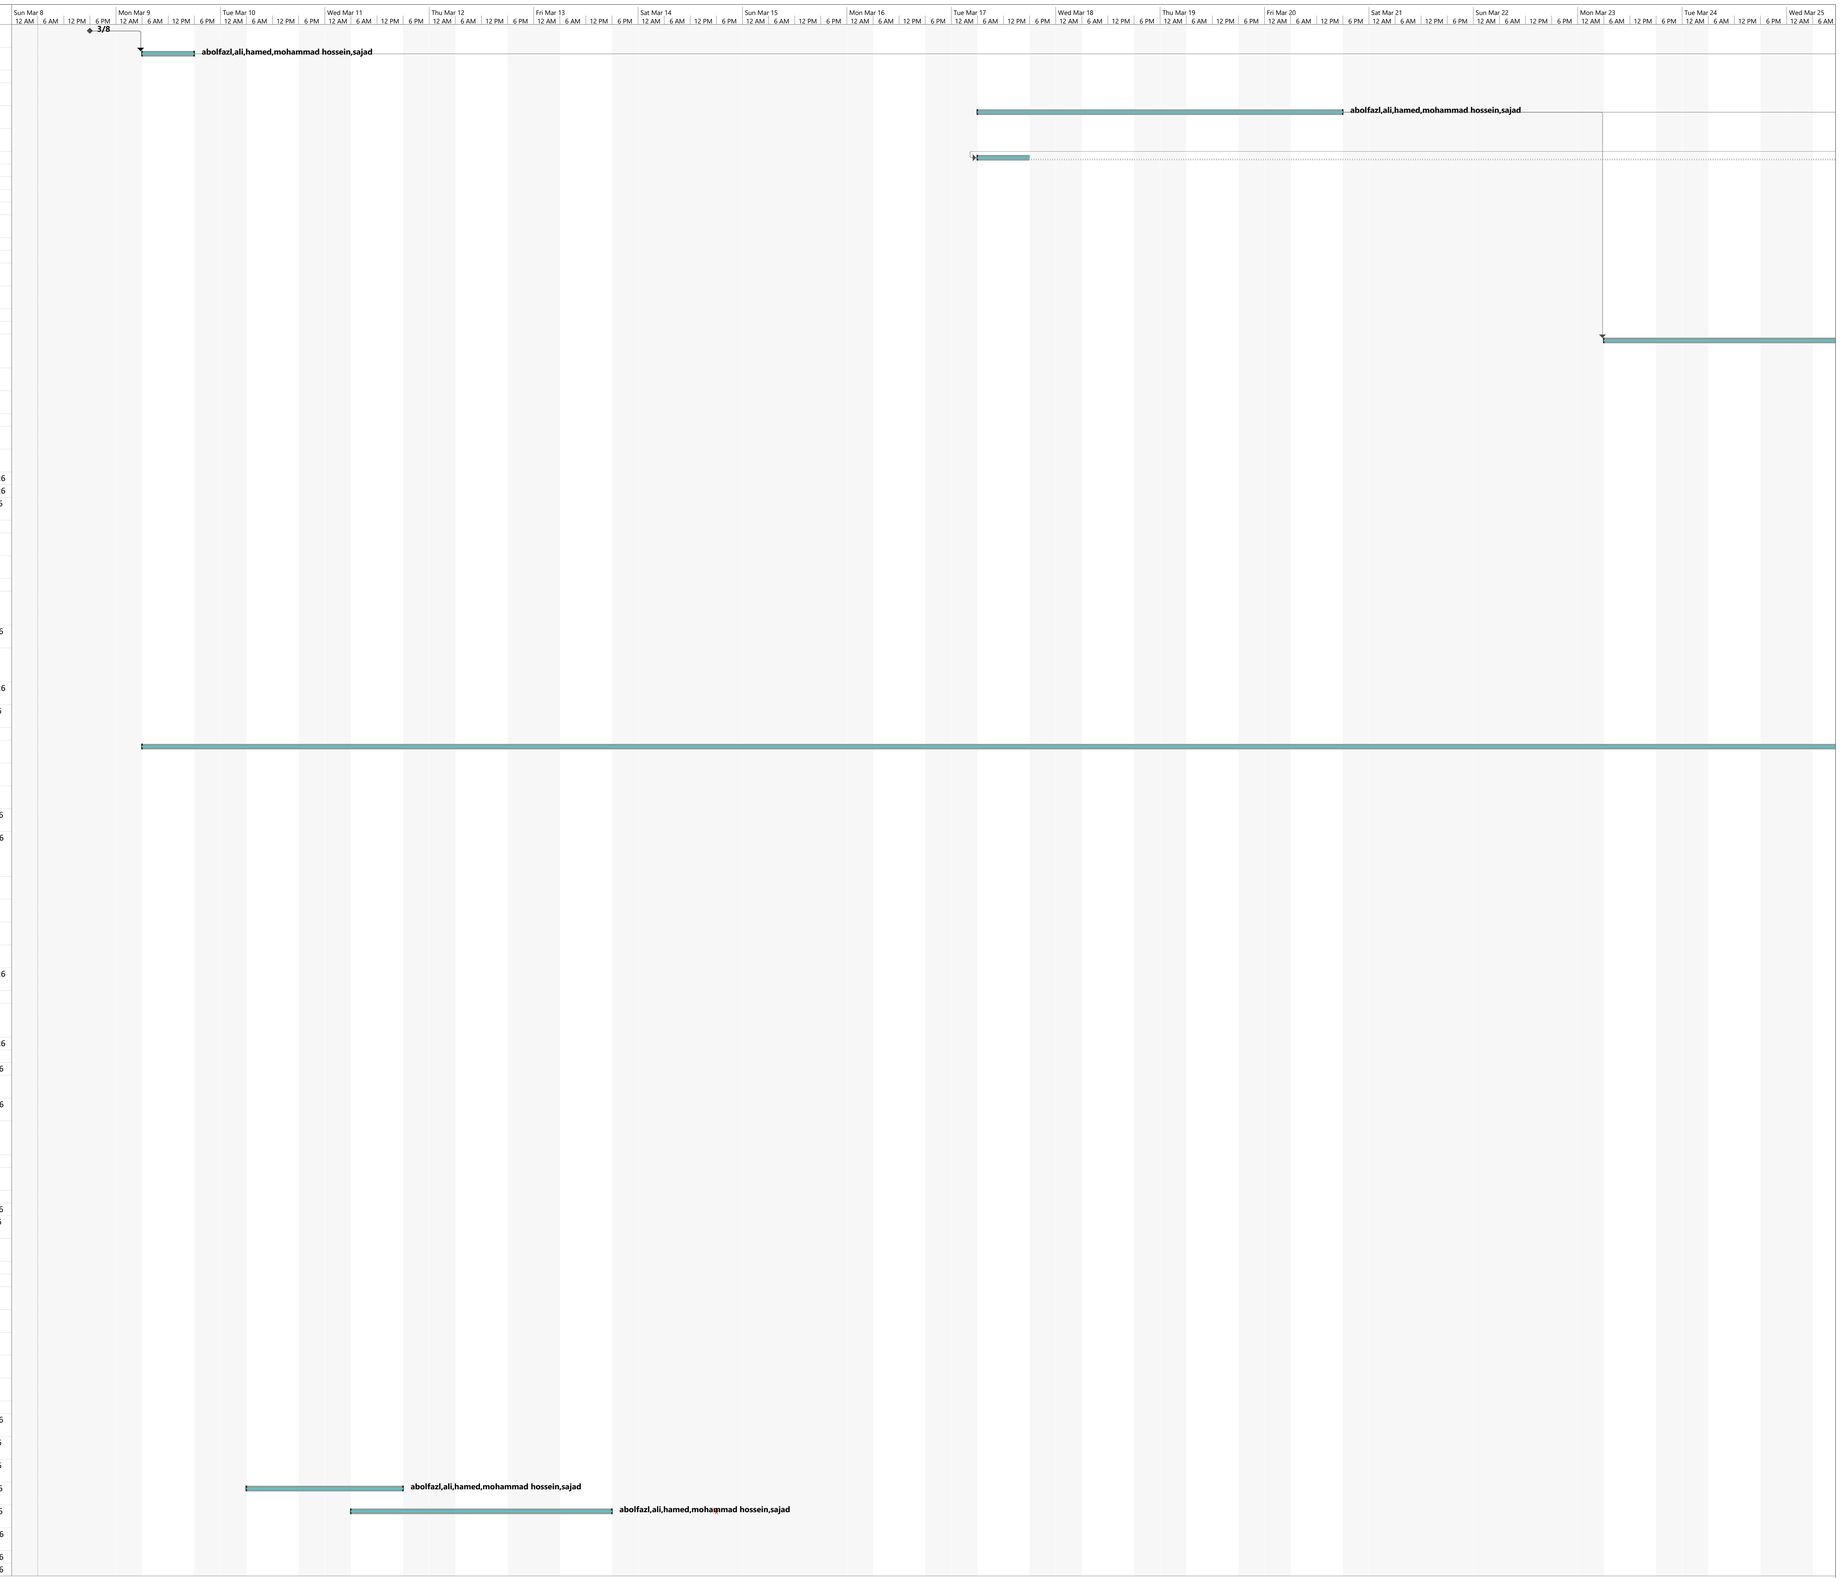

Project: ReserveCenter
Date: Thu 7/16/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

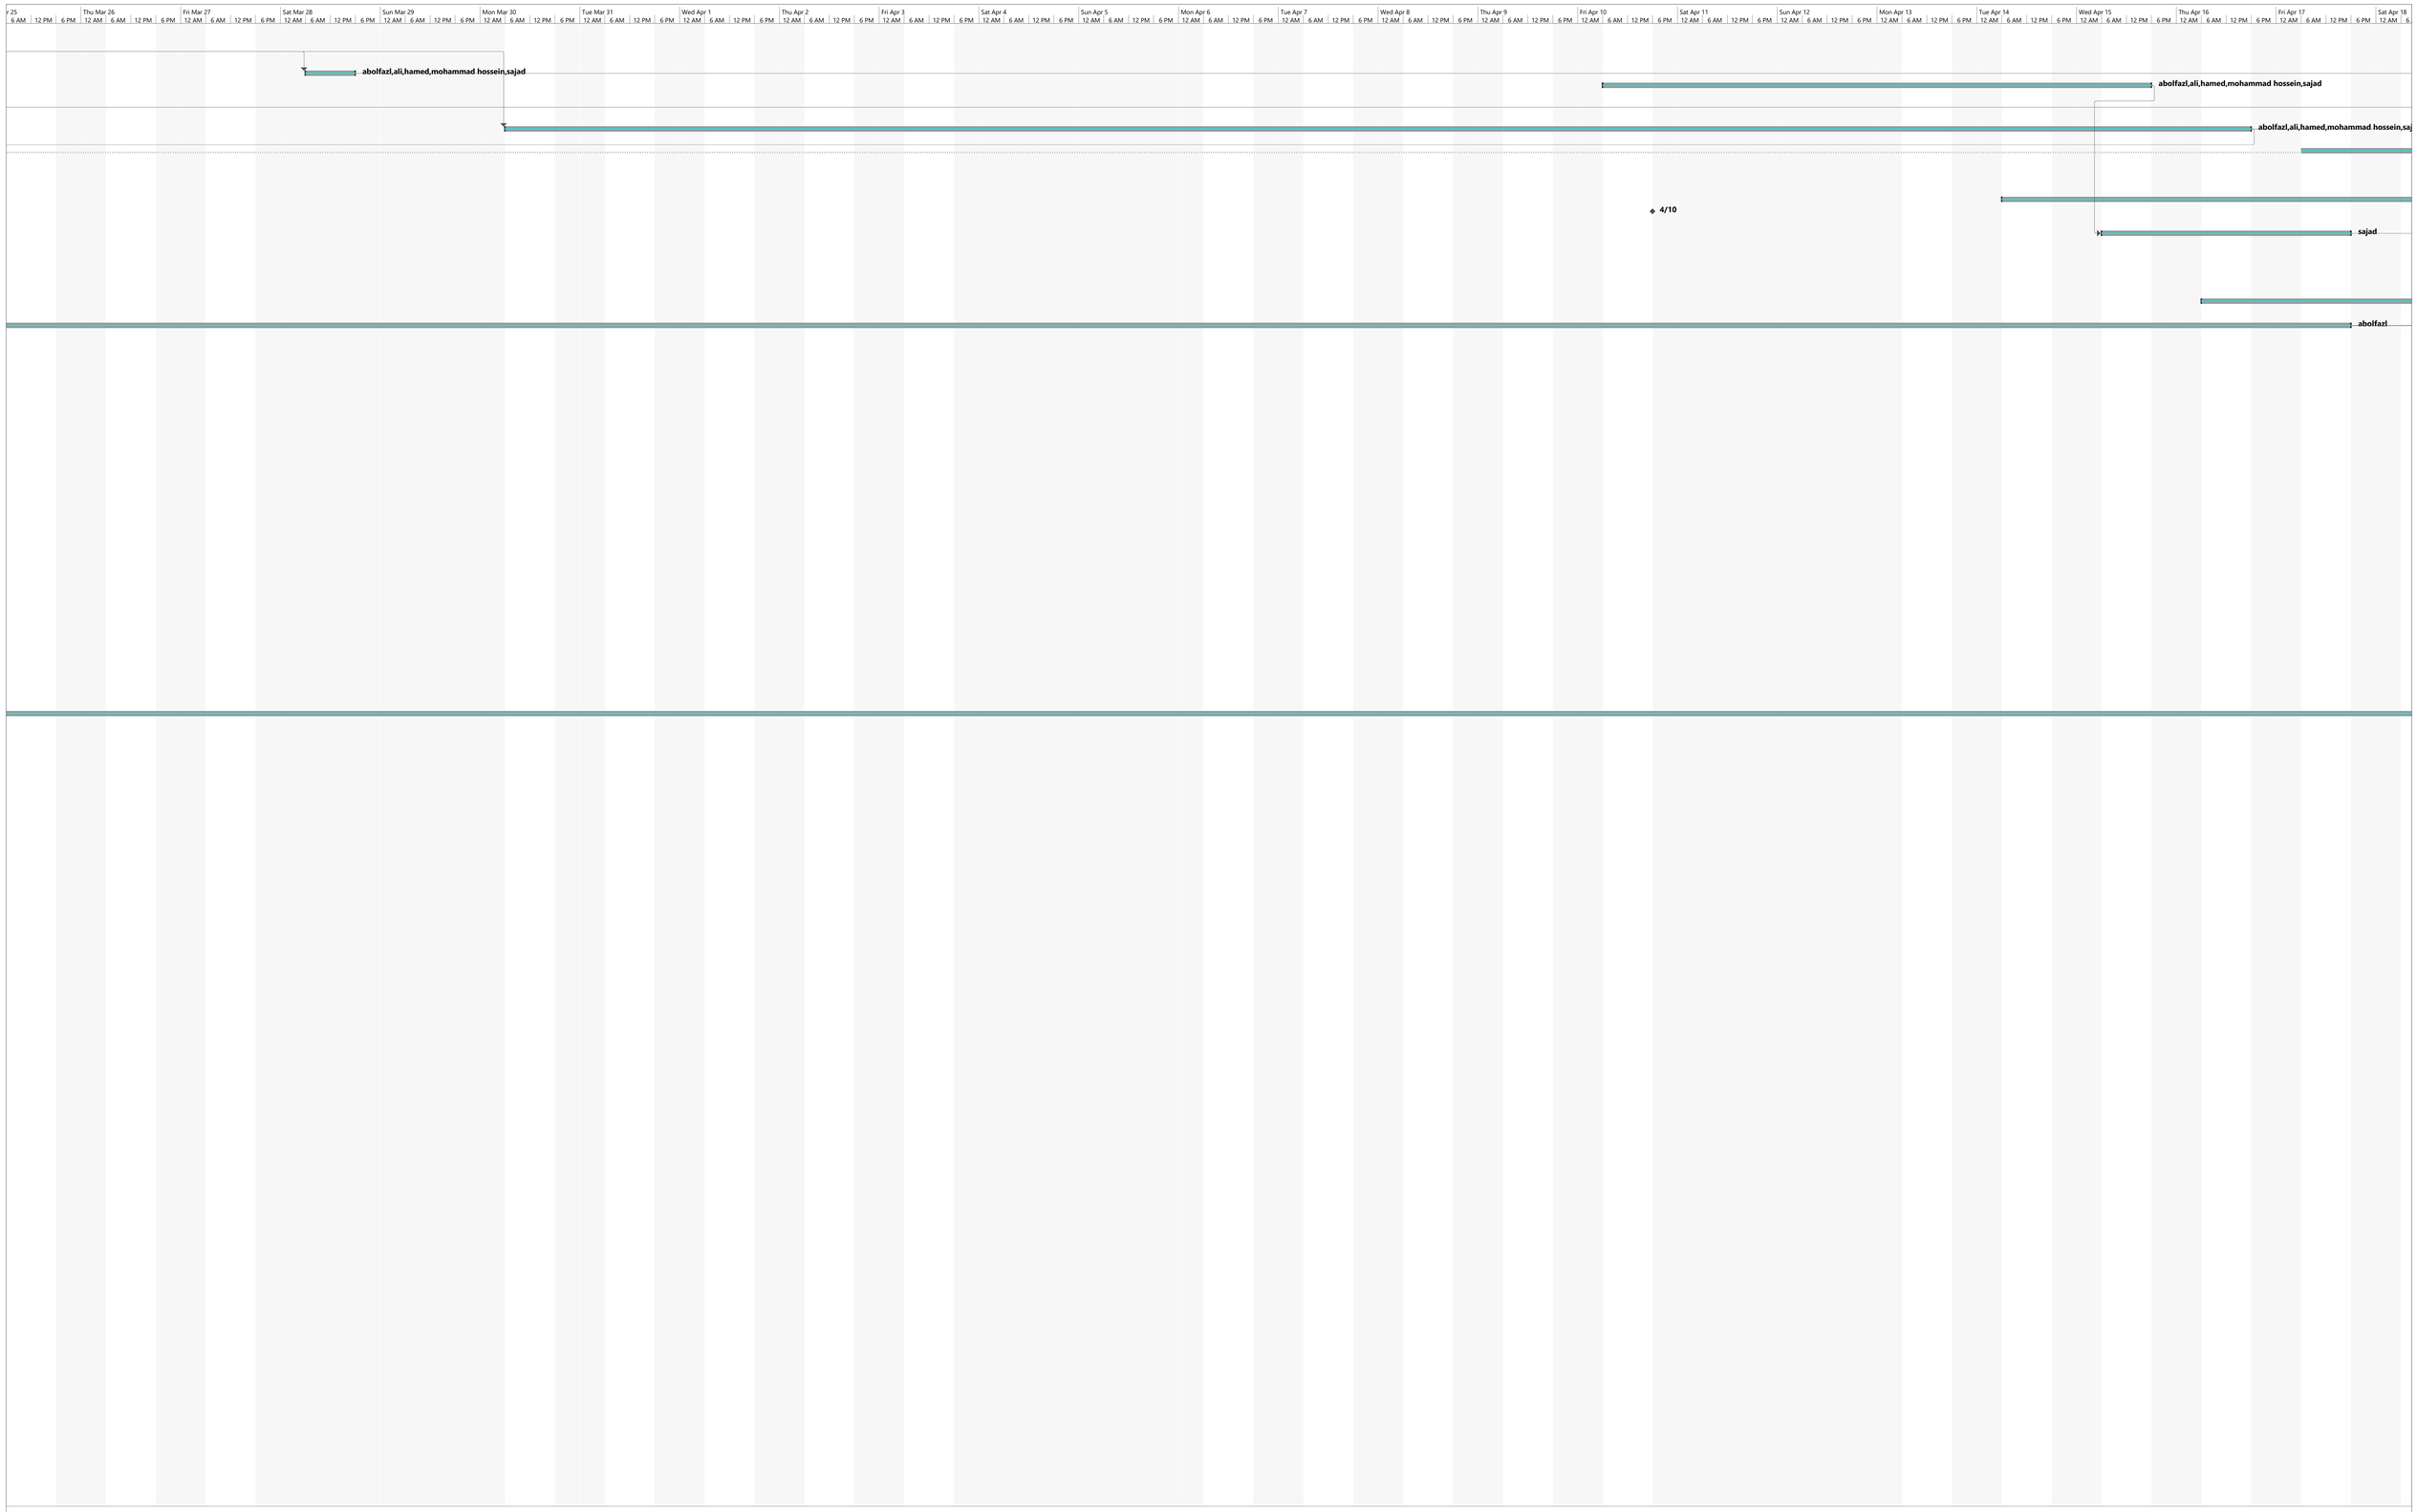

Project: ReserveCenter
Date: Thu 7/16/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

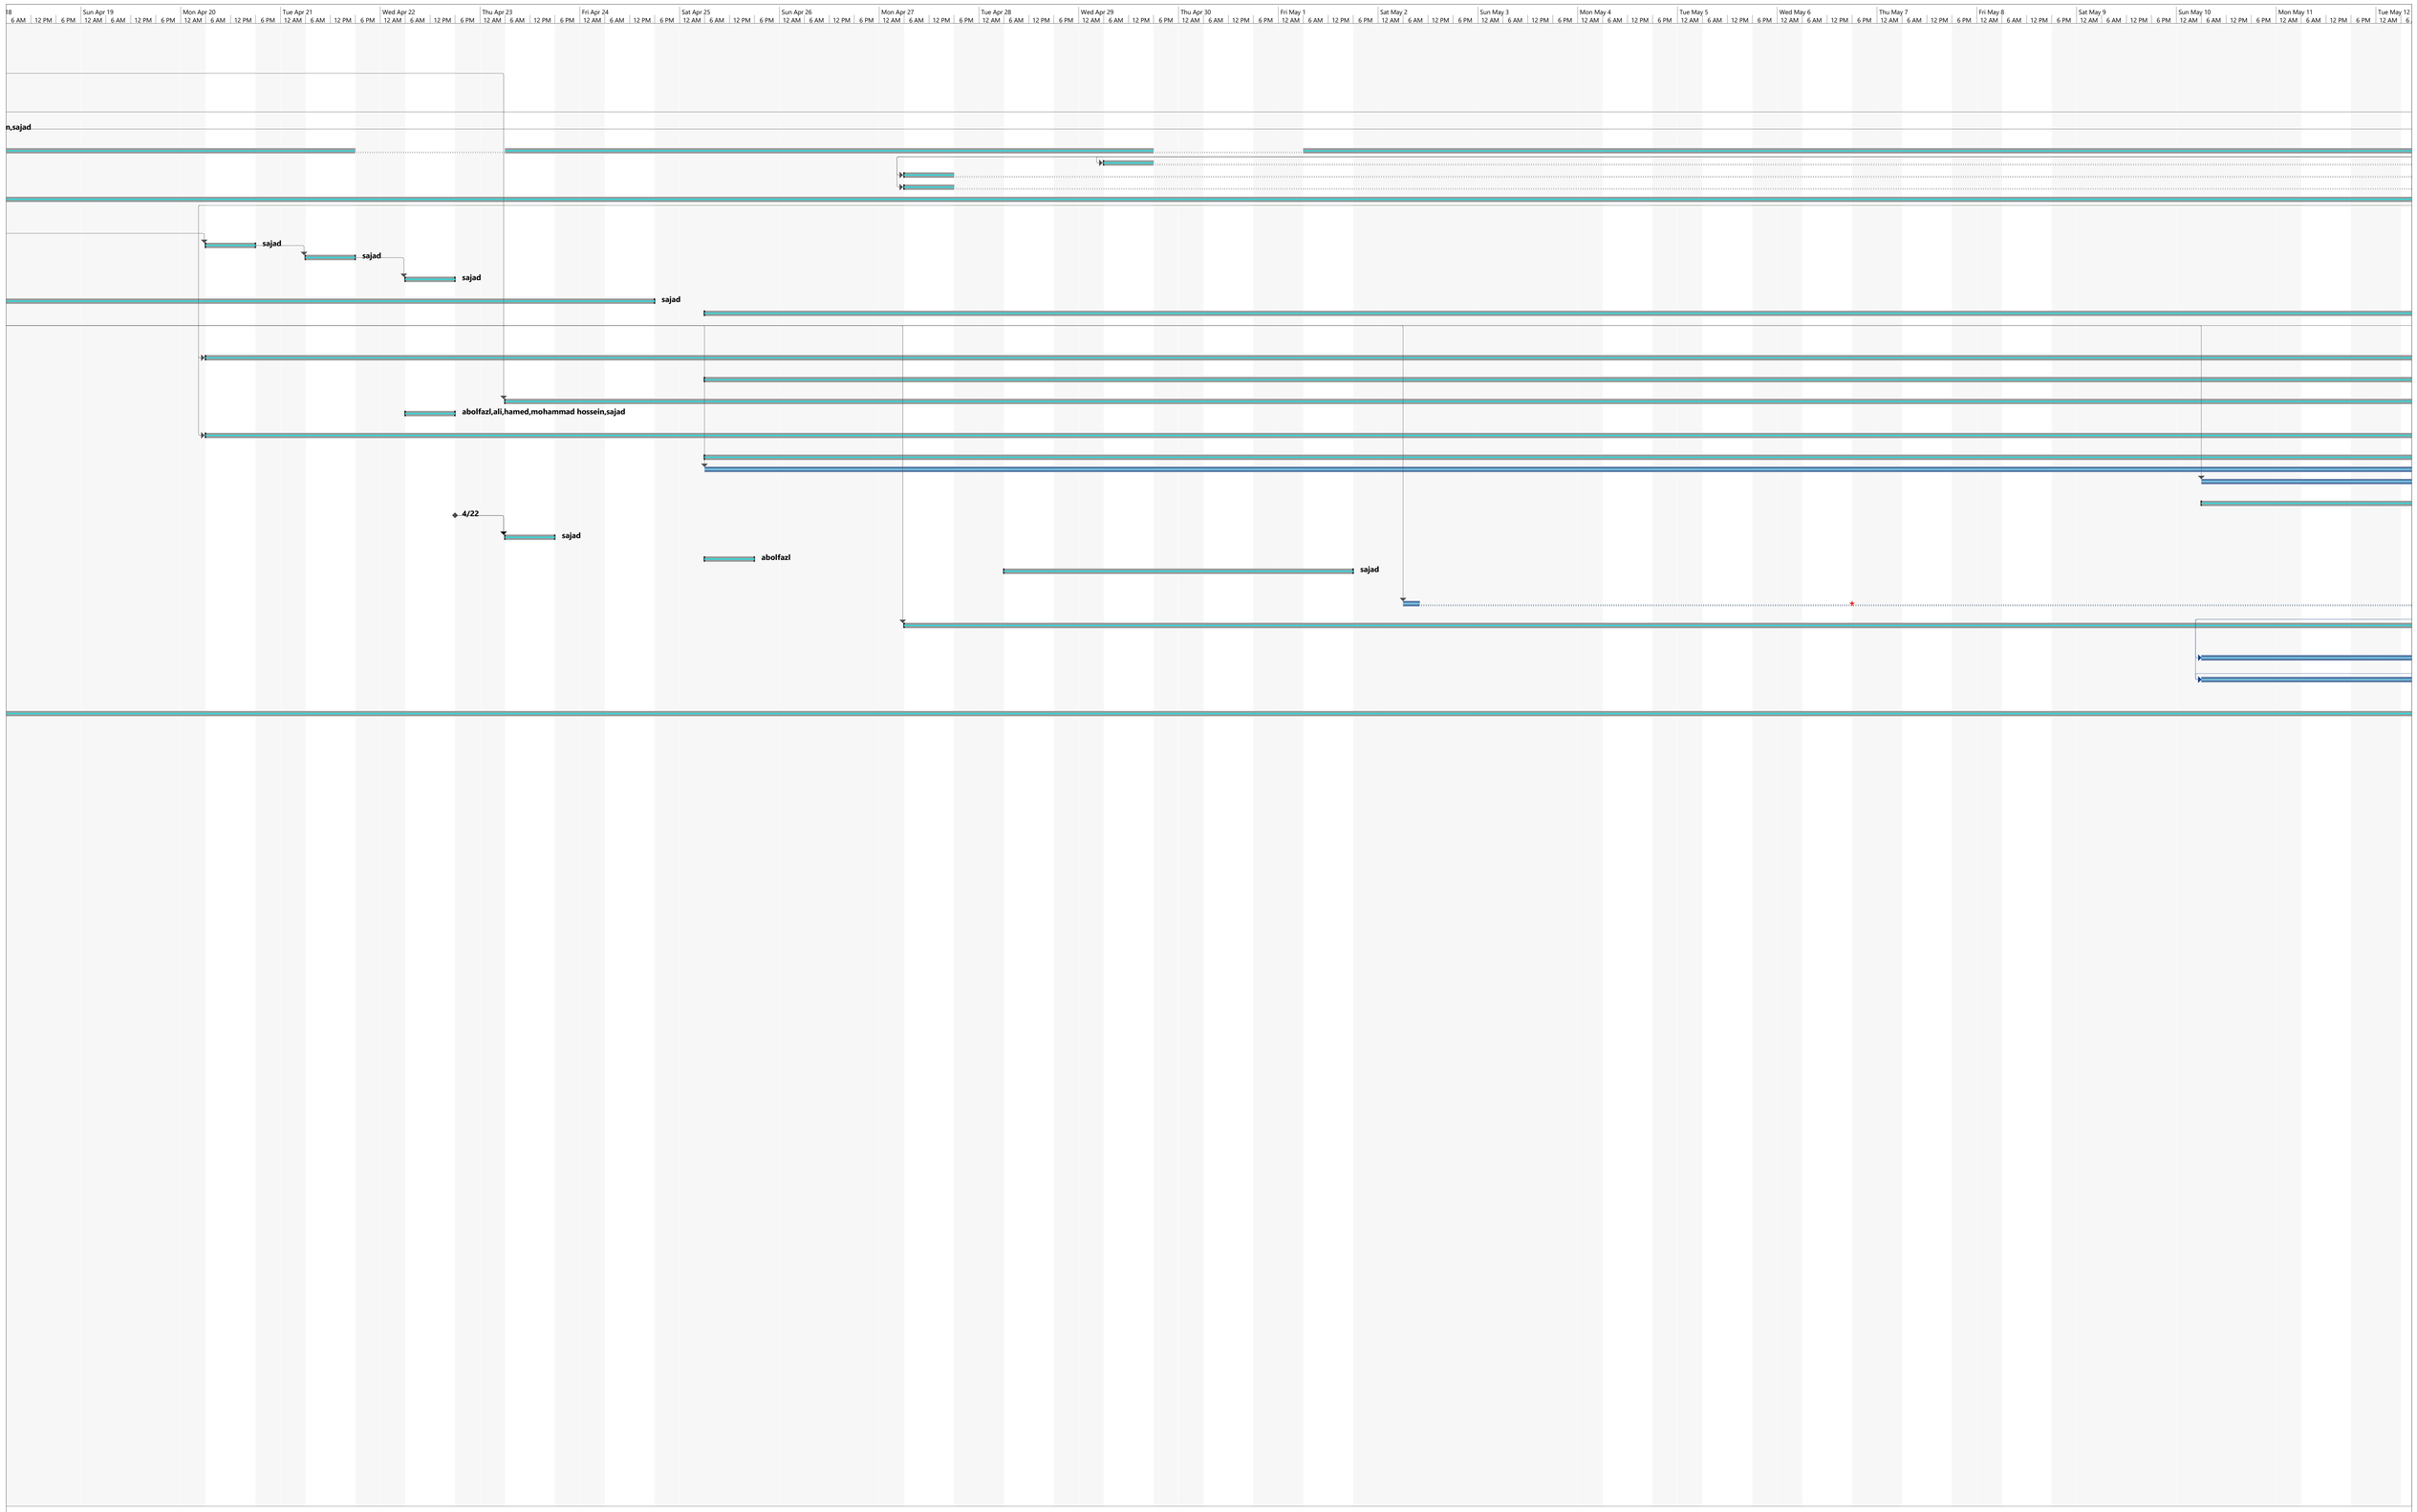

Project: ReserveCenter
Date: Thu 7/16/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

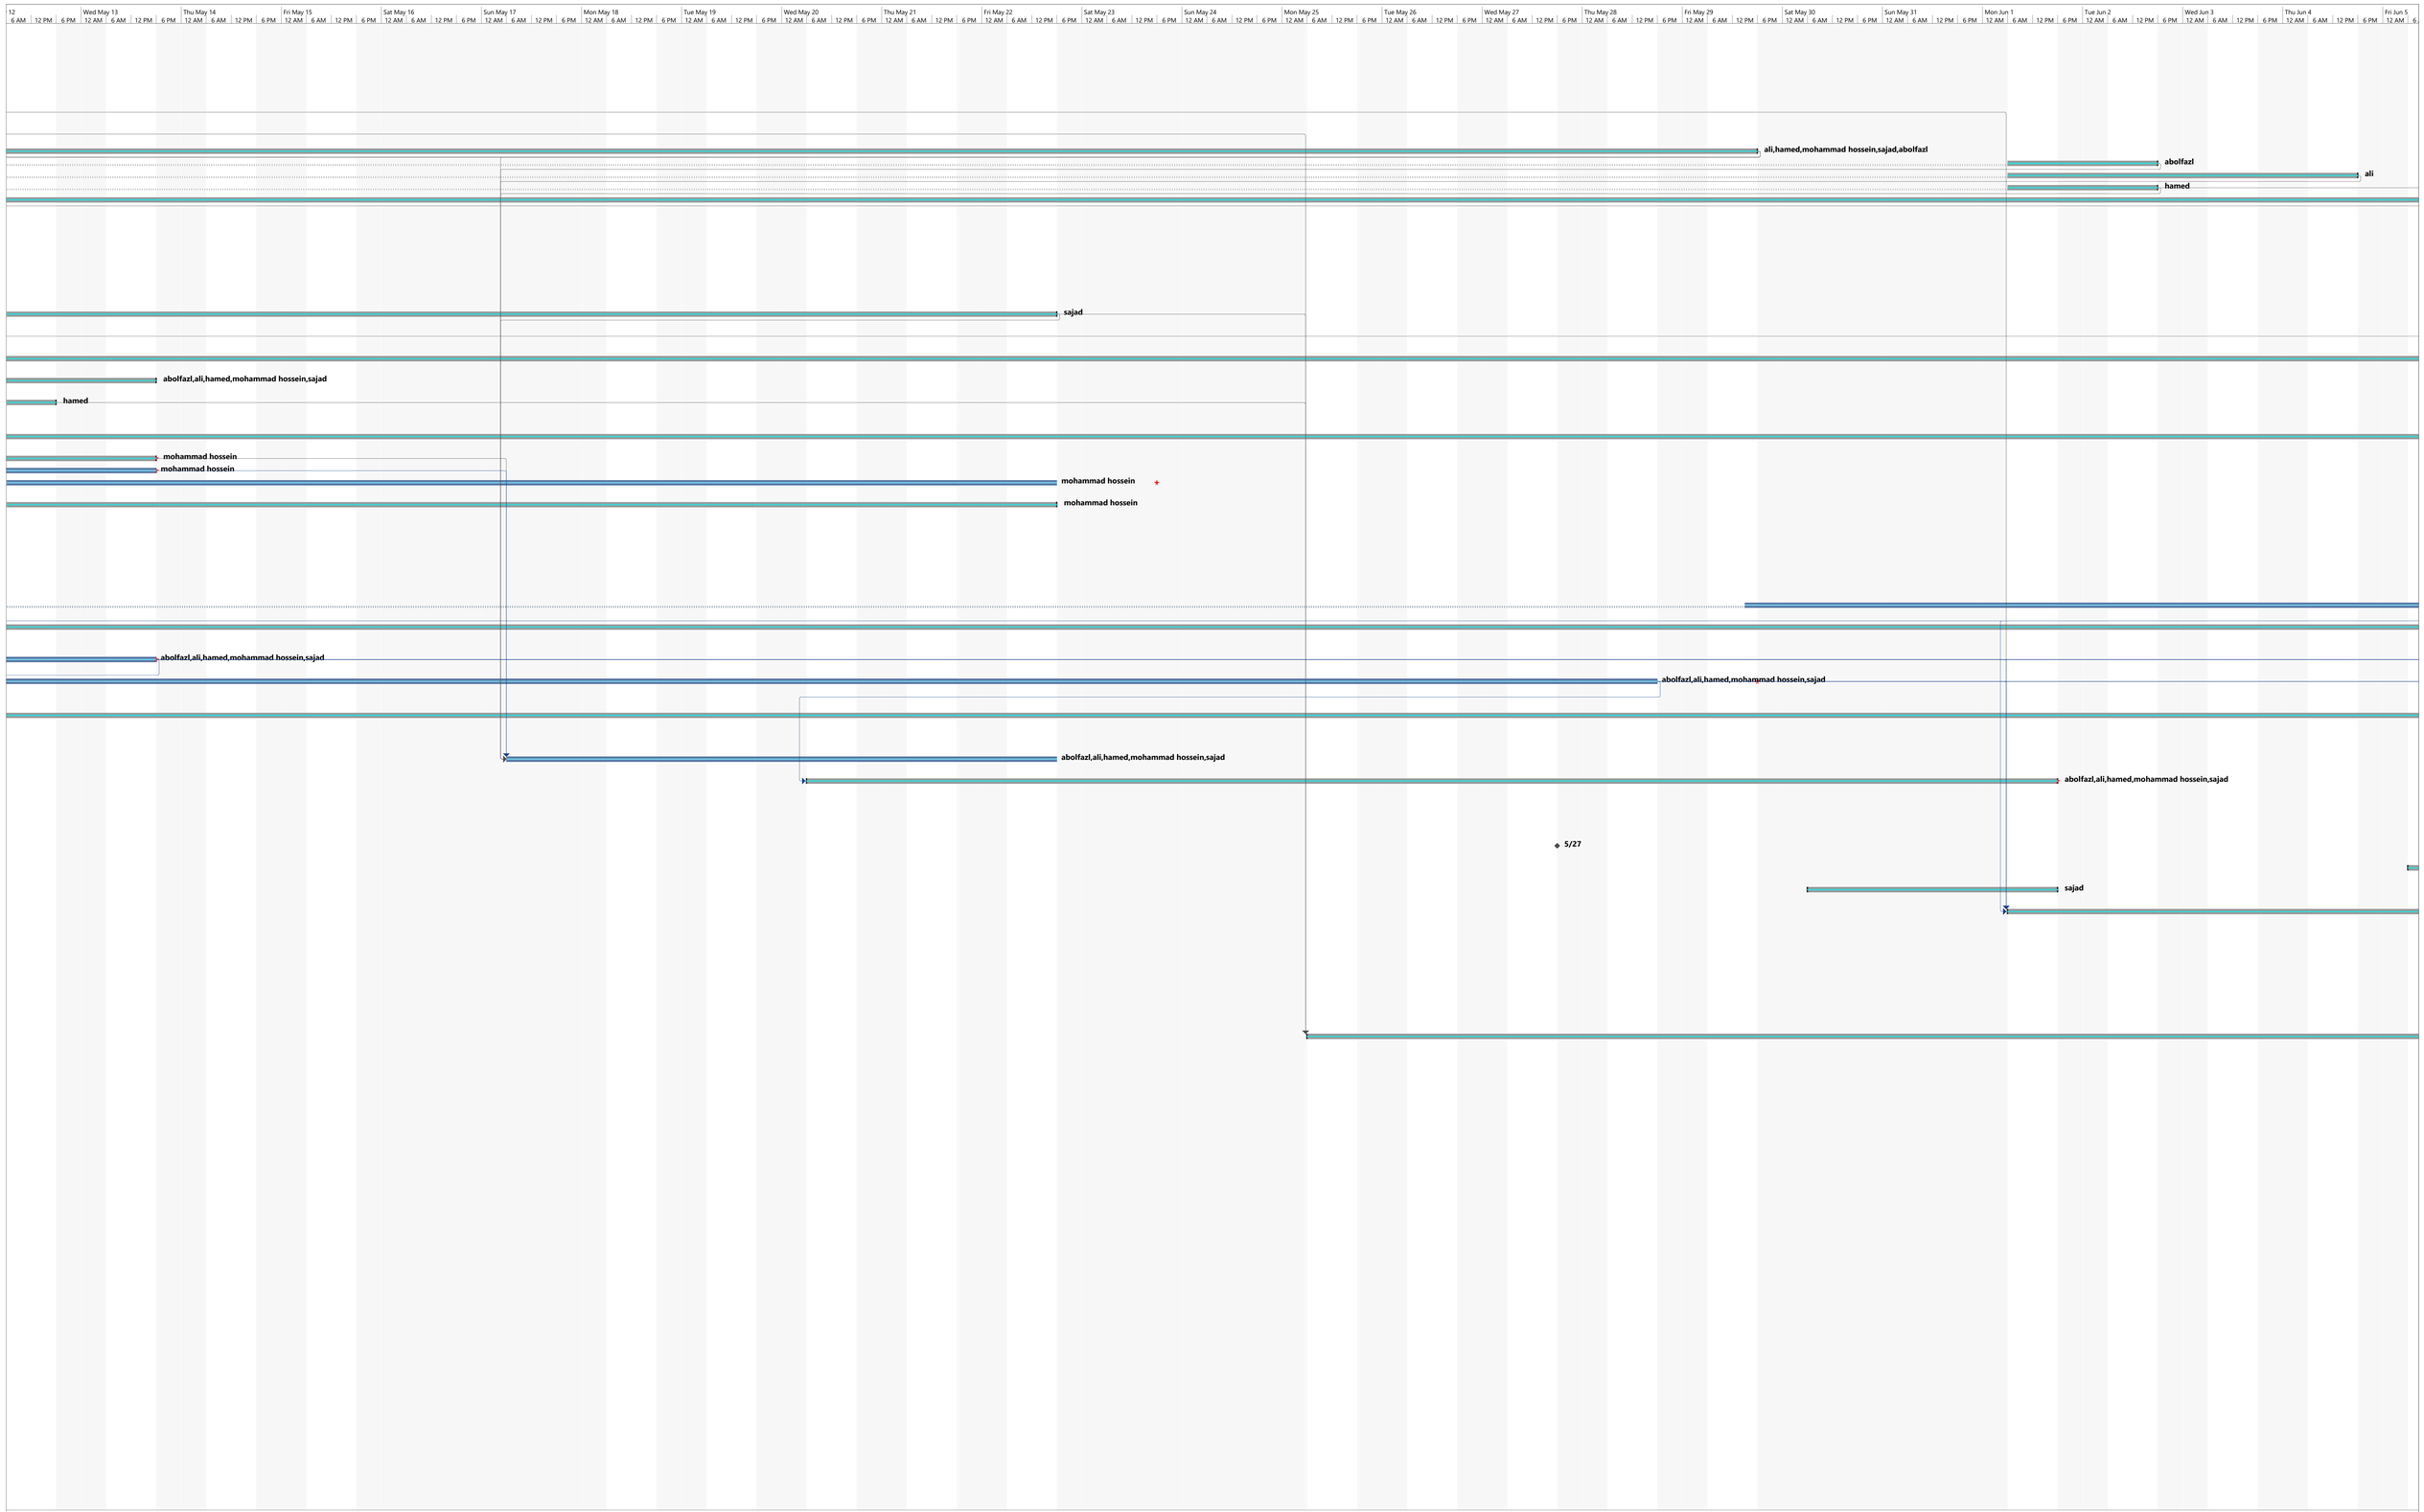

Project: ReserveCenter
Date: Thu 7/16/26

Task		Milestone		Project Summary		Inactive Milestone		Manual Task		Manual Summary Rollup		Start-only		External Tasks		Deadline		Manual Progress	
Split		Summary		Inactive Task		Inactive Summary		Duration-only		Manual Summary		Finish-only		External Milestone		Progress			

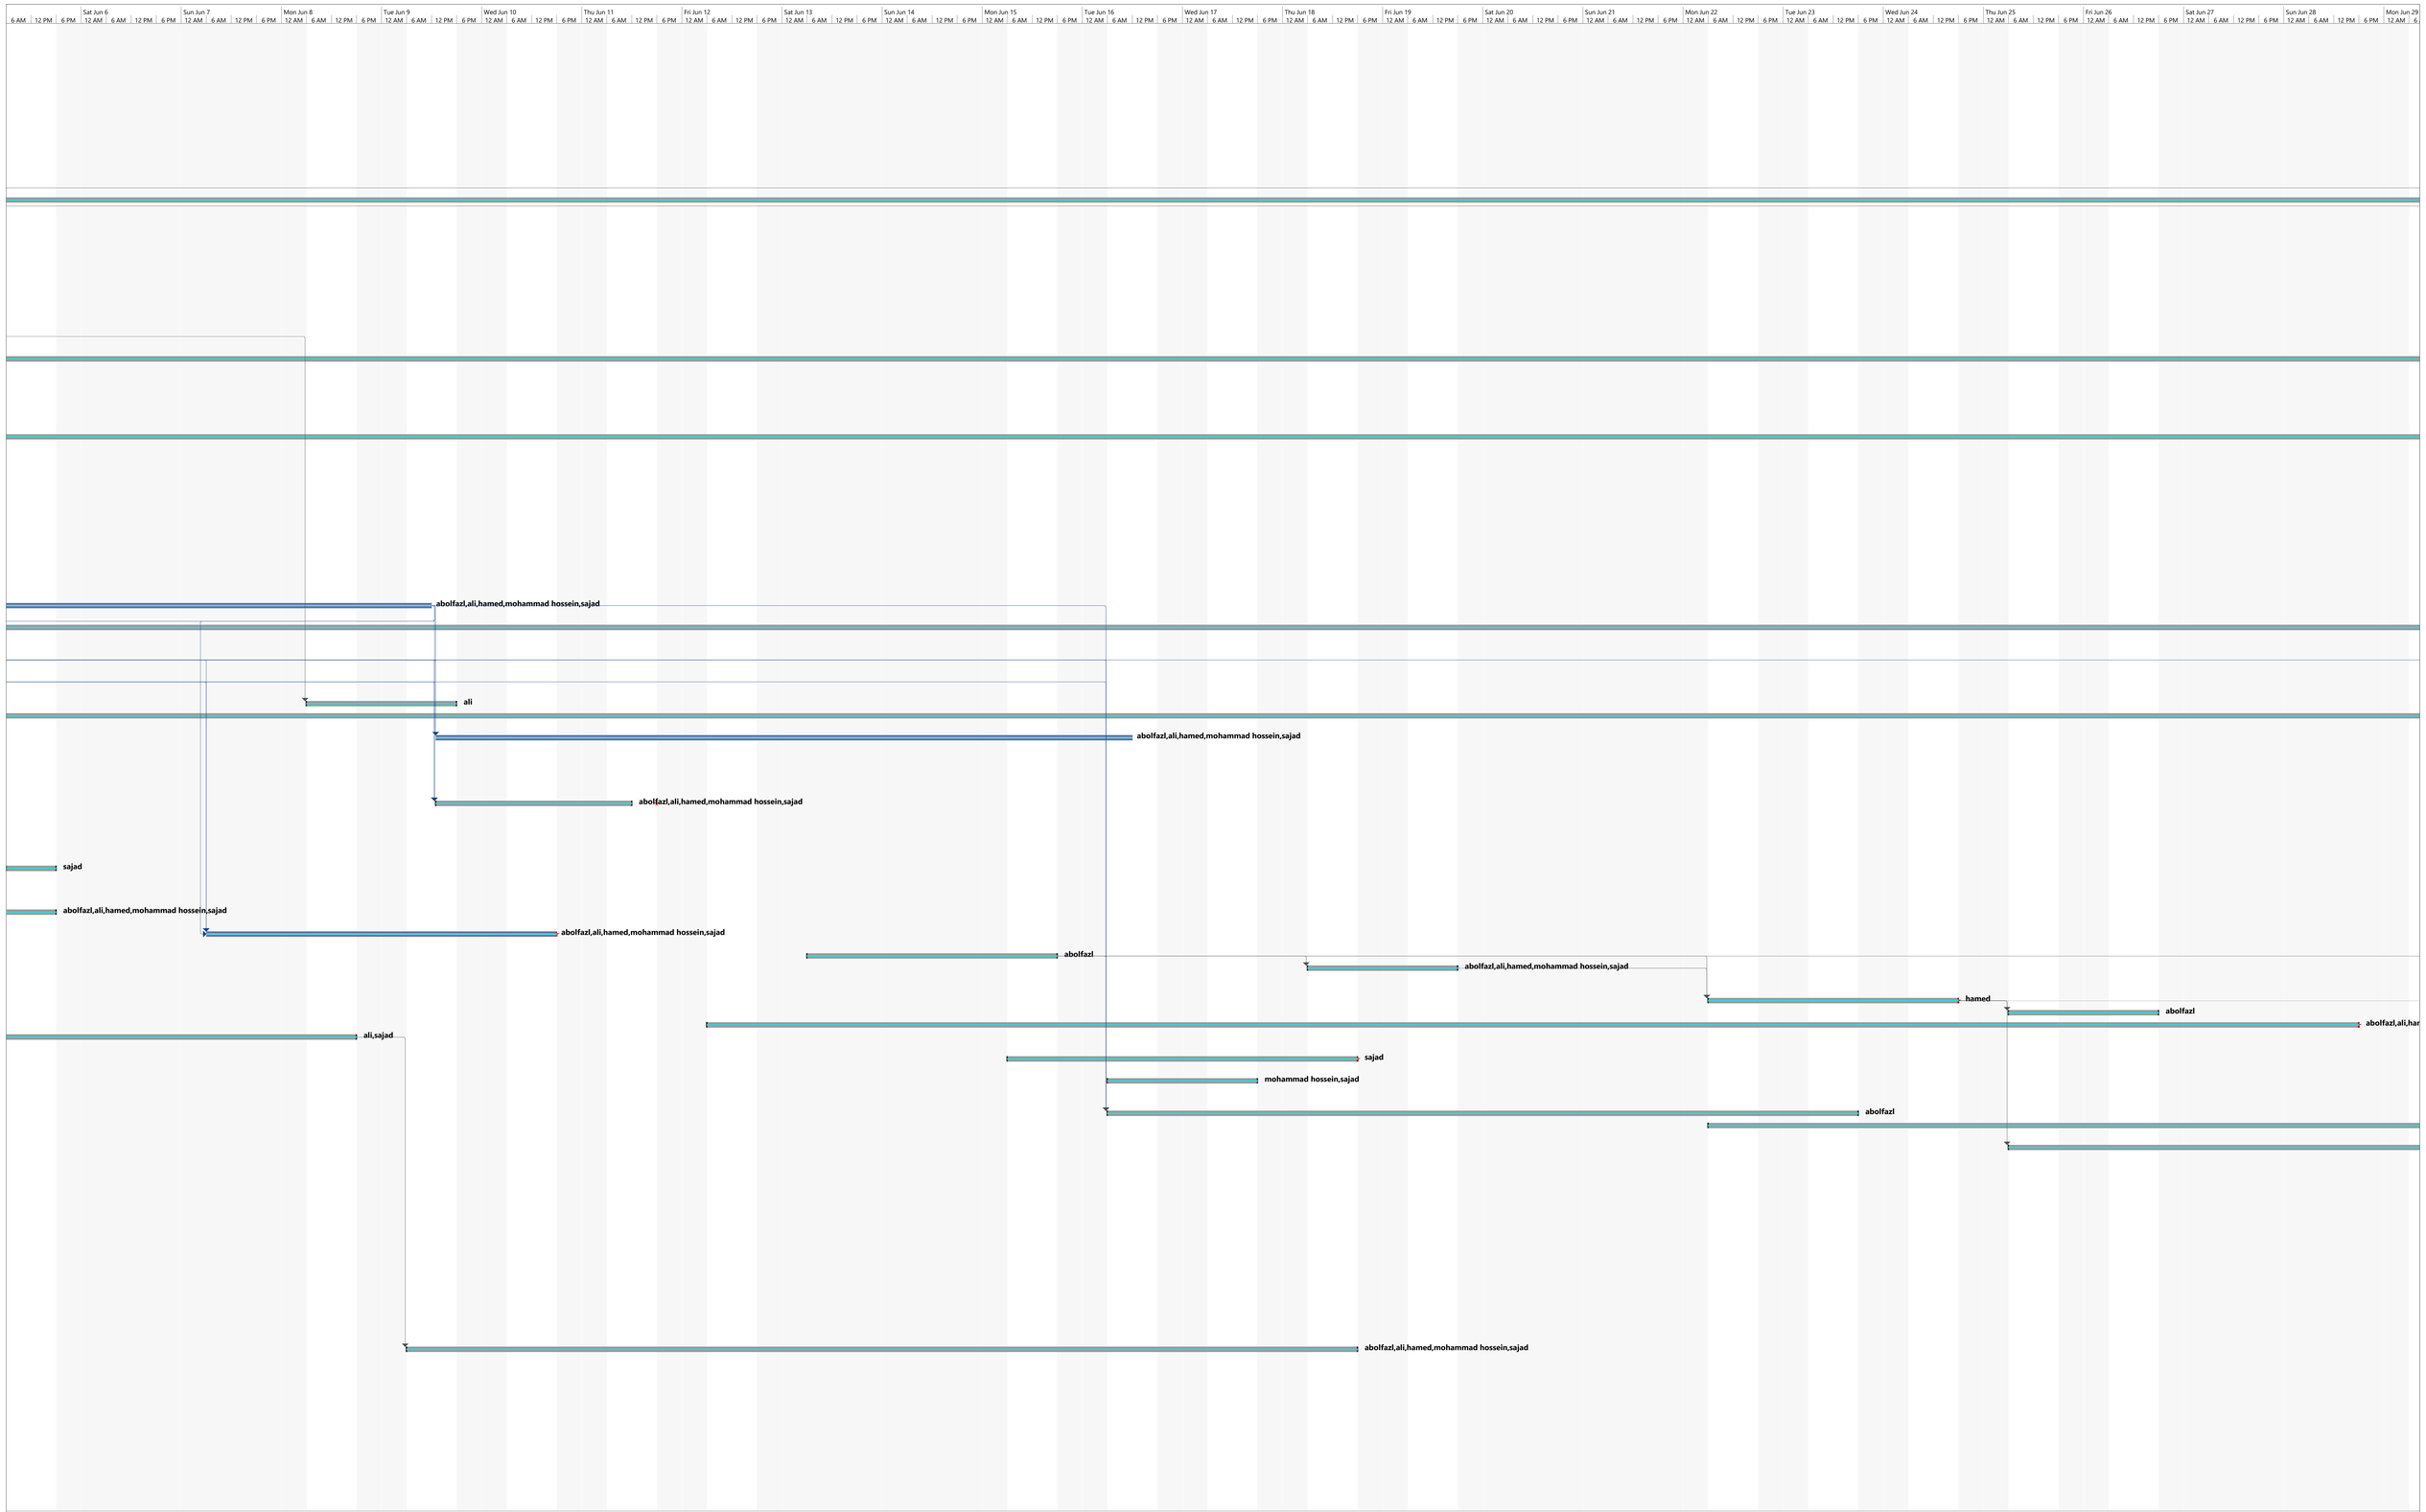

Project: ReserveCenter
Date: Thu 7/16/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress

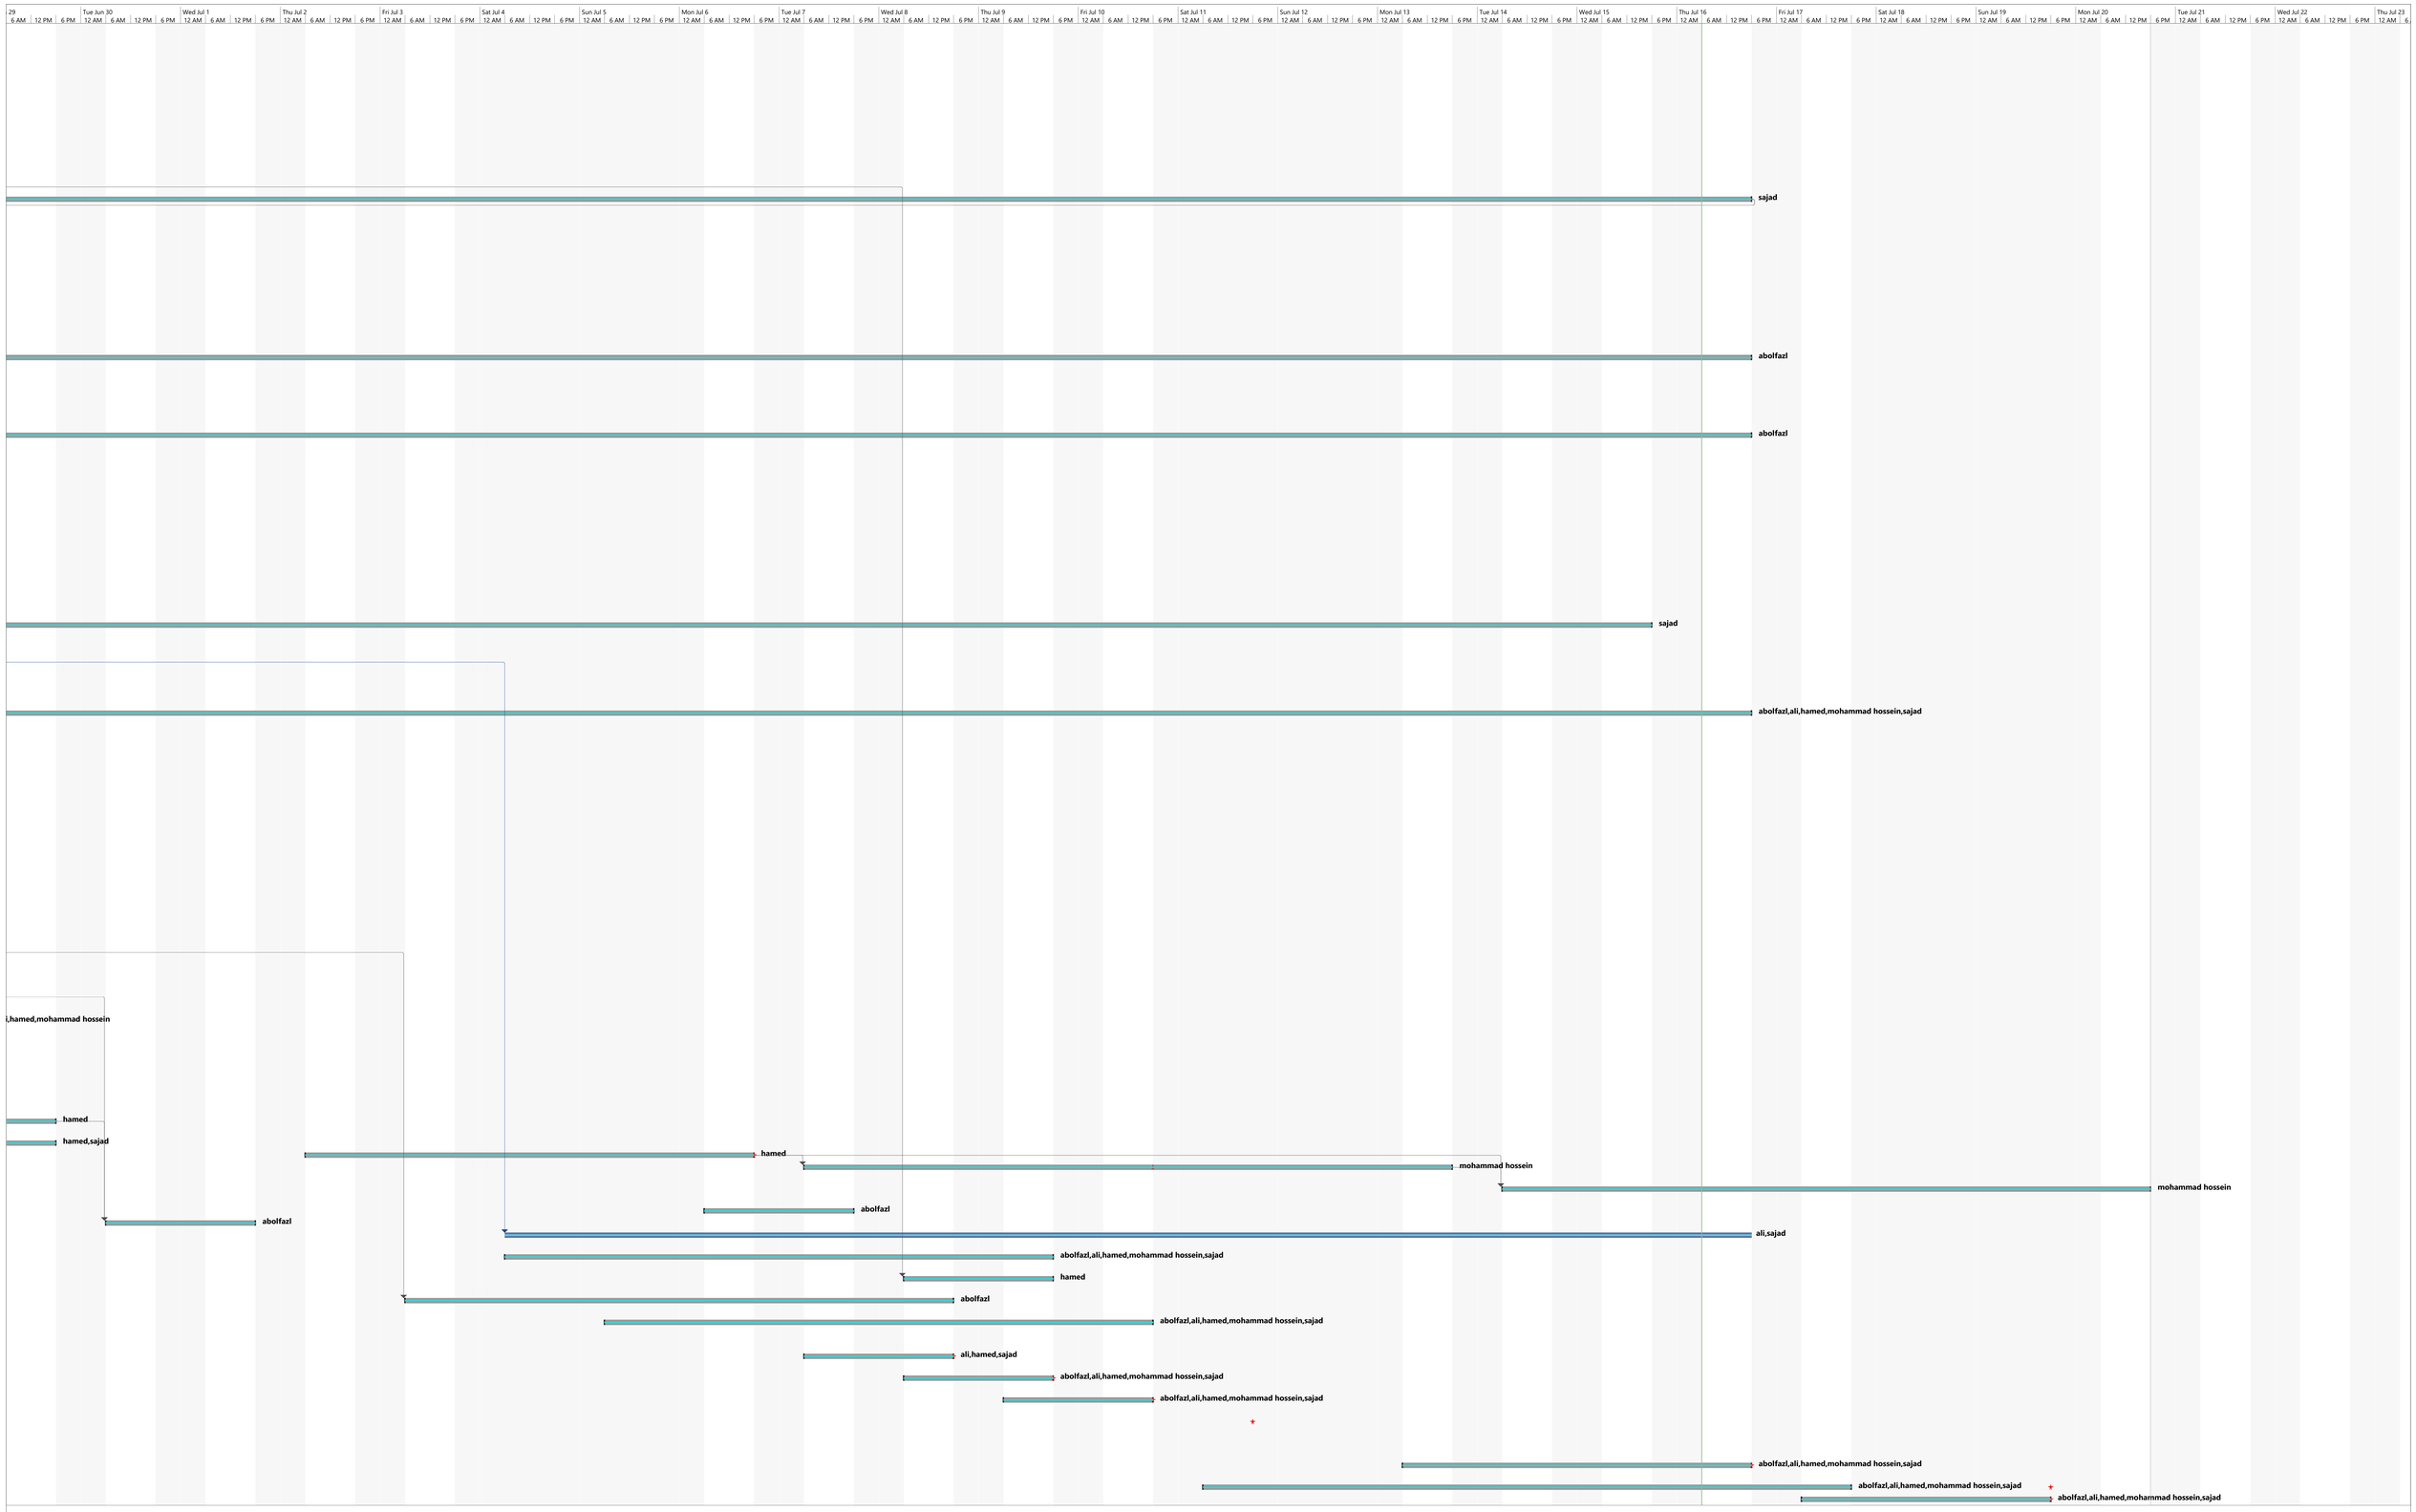

Project: ReserveCenter
Date: Thu 7/16/26

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
